

LAB 2

Agile Backlog Creation & Sprint Simulation in Jira

Project: Inter-City Freight Load Matching Marketplace

Jira Project: SE_LAB2 **Board:** IFLM board

NAME: SHRUTI CHOUDHARY
SRN: PES1UG24AM271

This submission documents the creation and prioritization of the Agile backlog, Fibonacci story-point estimation, two sprint simulations, and burndown analysis for the freight load matching marketplace.

Item	Result
Epics	5
User Stories	14
Total Story Points	63
Sprints Completed	2
Sprint 1 Planned Points	27
Sprint 2 Planned Points	36

1. Agile Backlog

The backlog was created from the functional requirements of the Inter-City Freight Load Matching Marketplace. The work was organized into five logical epics covering account verification, freight posting/bidding, shipment tracking, payment settlement, and system reliability.

Backlog evidence from Jira

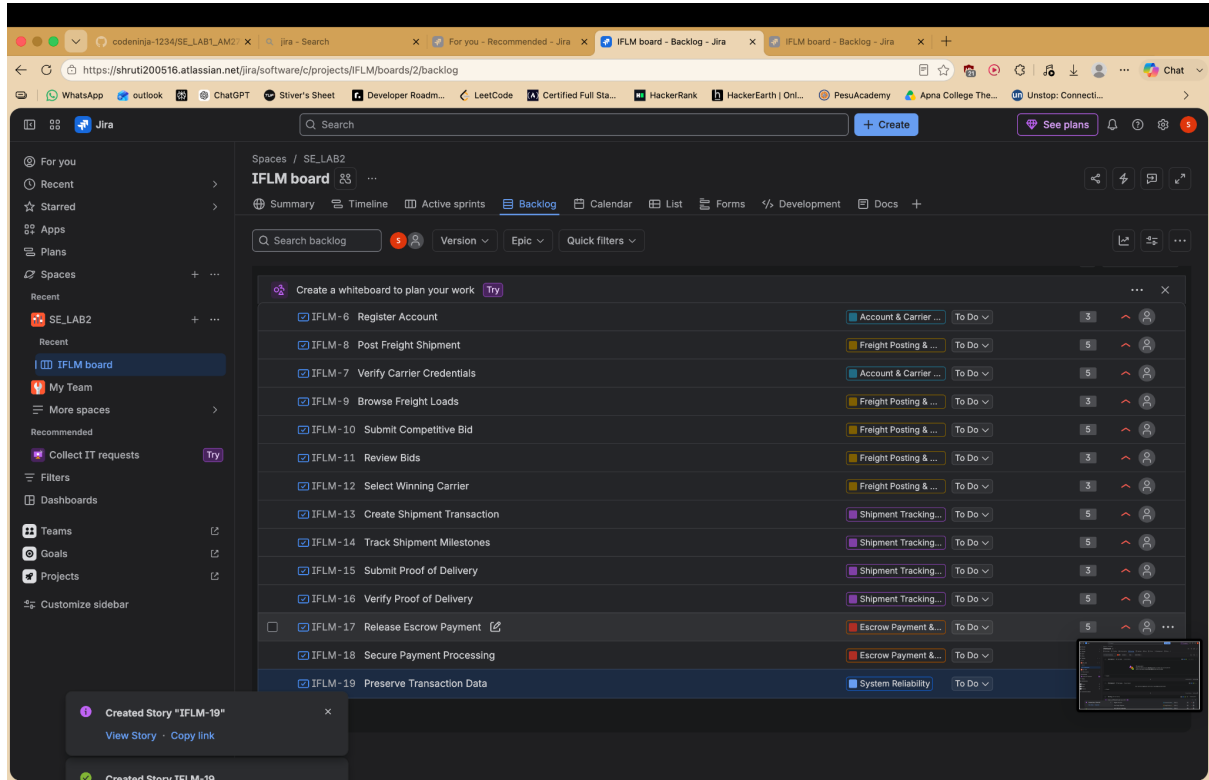


Figure 1. Jira backlog showing the 14 user stories, their parent epics, priorities/status, and assigned Fibonacci story points.

2. Story Point Assignments

Fibonacci story points were used as a relative estimate of complexity, effort, and uncertainty. The estimates range from 3 to 8 points for the implemented backlog items.

Epic	Key	User Story	Priority	Points
Account & Carrier Verification	IFLM-6	Register Account	High	3
Account & Carrier Verification	IFLM-7	Verify Carrier Credentials	High	5
Freight Posting & Competitive Bidding	IFLM-8	Post Freight Shipment	High	5
Freight Posting & Competitive Bidding	IFLM-9	Browse Freight Loads	High	3
Freight Posting & Competitive Bidding	IFLM-10	Submit Competitive Bid	High	5
Freight Posting & Competitive Bidding	IFLM-11	Review Bids	High	3
Freight Posting & Competitive Bidding	IFLM-12	Select Winning Carrier	High	3
Shipment Tracking & Delivery	IFLM-13	Create Shipment Transaction	High	5
Shipment Tracking & Delivery	IFLM-14	Track Shipment Milestones	High	5
Shipment Tracking & Delivery	IFLM-15	Submit Proof of Delivery	High	3
Shipment Tracking & Delivery	IFLM-16	Verify Proof of Delivery	High	5
Escrow Payment & Settlement	IFLM-17	Release Escrow Payment	High	5
Escrow Payment & Settlement	IFLM-18	Secure Payment Processing	High	5
System Reliability	IFLM-19	Preserve Transaction Data	High	8
		TOTAL		63

Estimation approach: Smaller, more straightforward activities such as registration, browsing, reviewing, and carrier selection were estimated at 3 points. Verification, transaction, tracking, proof-of-delivery, and payment functions were generally 5 points. Preserving critical transaction data was estimated at 8 points because of its broader reliability and data-integrity responsibility.

3. Sprint 1 Simulation

Goal: Complete account verification and core freight bidding functionality.

Scope: Register Account (3), Verify Carrier Credentials (5), Post Freight Shipment (5), Browse Freight Loads (3), Submit Competitive Bid (5), Review Bids (3), and Select Winning Carrier (3). **Total: 27 points.**

Sprint board evidence

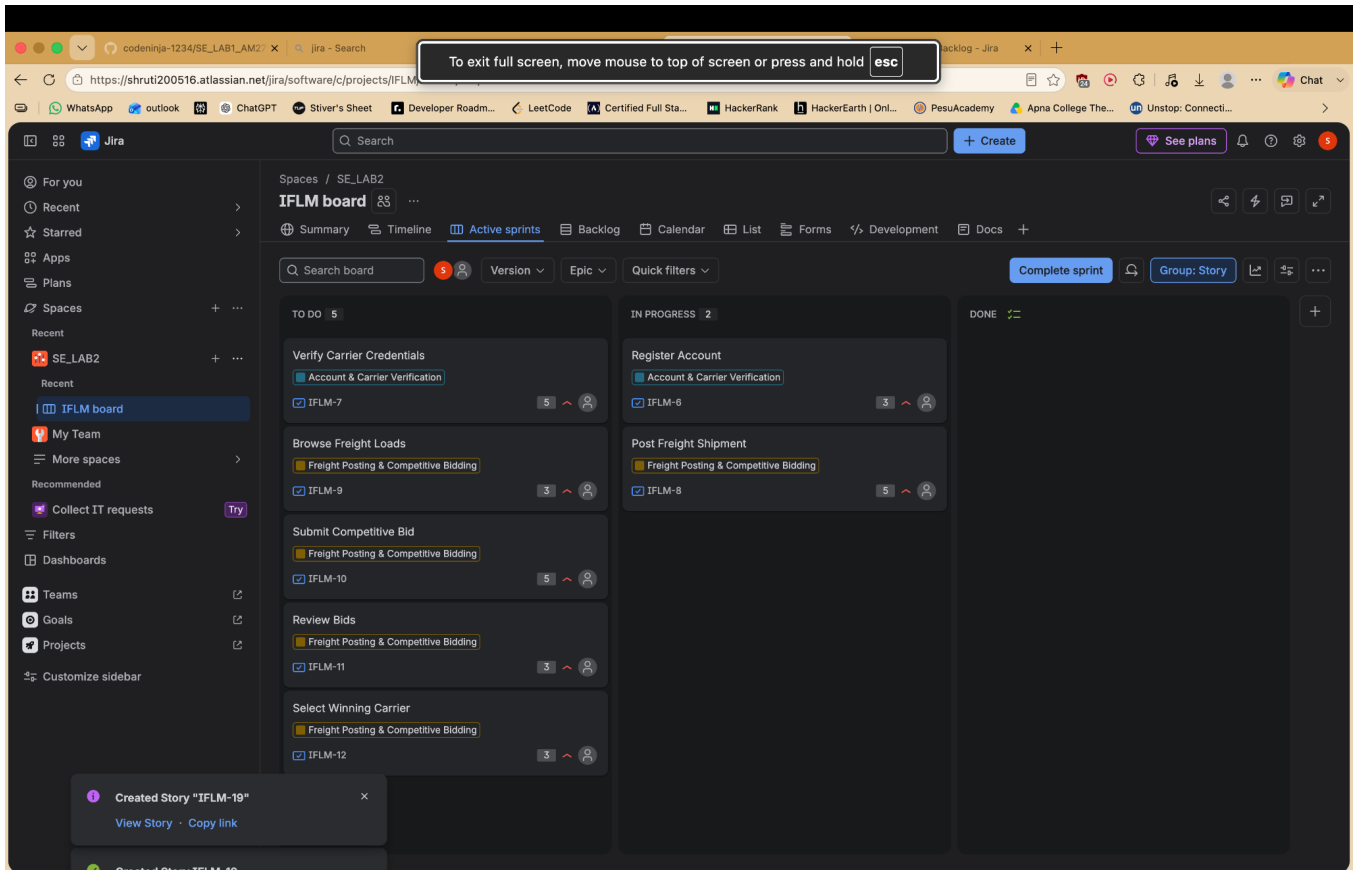


Figure 2. Sprint 1 active-sprint board during the simulation, showing the planned work moving through To Do and In Progress toward Done.

The sprint work was simulated by moving stories through the Jira workflow: To Do → In Progress → Done. The planned Sprint 1 scope was 27 story points.

4. Sprint 2 & Burndown Chart

Goal: Complete shipment tracking, delivery verification, and secure payment functionality.

Scope: Create Shipment Transaction (5), Track Shipment Milestones (5), Submit Proof of Delivery (3), Verify Proof of Delivery (5), Release Escrow Payment (5), Secure Payment Processing (5), and Preserve Transaction Data (8). **Total: 36 points.**

Burndown evidence

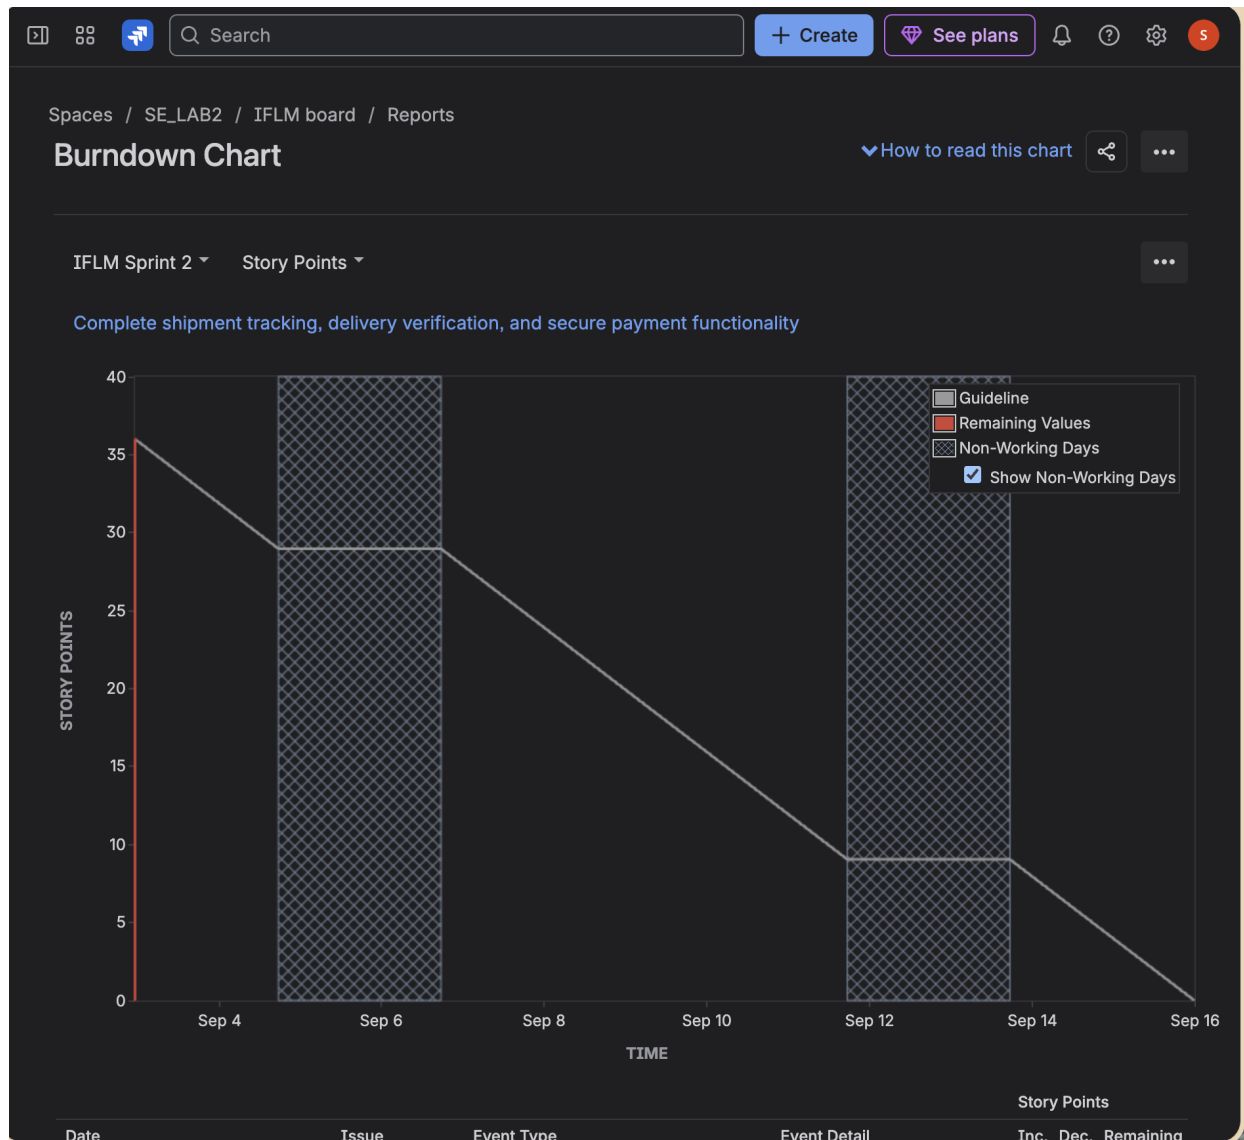


Figure 3. Jira Burndown Chart for IFLM Sprint 2 using Story Points. The remaining work falls from 36 points to 0 points.

The chart shows the planned guideline and the remaining work. Because this was a simulated exercise, the completion occurred rapidly; nevertheless, the report records the sprint scope and its reduction to zero.

5. Sprint Completion Evidence

The Jira burndown event log records the Sprint 2 start with 36 points and successive issue completions that reduced the remaining work to 31, 26, 23, 18, 13, 8, and finally 0 points.

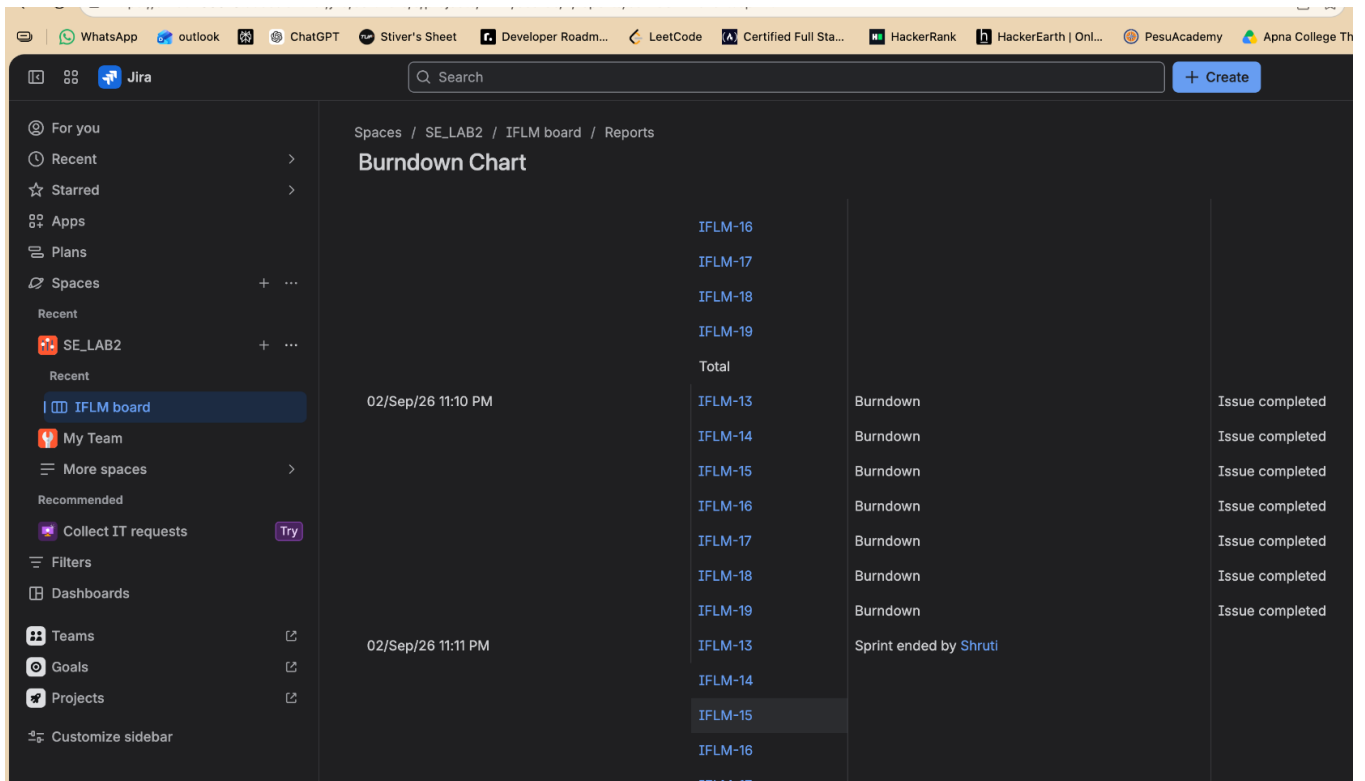


Figure 4. Jira burndown event details showing issue completions and the remaining story points reaching 0.

6. Reflection

1. Did your estimations reflect actual effort?

The estimates were reasonable as relative measures of effort. Simpler marketplace activities were assigned 3 points, while verification, tracking, payment, and transaction-related activities were mostly 5 points, and the broader data-preservation requirement was 8 points. Since the sprint was simulated rather than performed as a real development cycle, actual effort cannot be compared quantitatively with high confidence.

2. Was your backlog well-prioritized?

Yes. The backlog was prioritized around the core marketplace workflow. Account verification and the main freight posting/bidding capabilities were treated as high-priority work, followed by shipment tracking, proof of delivery, payment settlement, and reliability concerns. Grouping the stories into five epics also made the backlog easier to understand and manage.

3. How did your simulated sprint align with your plan?

Sprint 1 focused on account verification and core bidding functionality and contained 27 planned points. Sprint 2 covered shipment creation/tracking, proof of delivery, payment, and reliability and contained 36 planned points. The two-sprint structure therefore matched the planned functional progression of the system.

4. What insights did the burndown chart give about your team's capacity?

The burndown chart showed how quickly the remaining workload decreased during the simulation and confirmed that the Sprint 2 scope reached zero remaining points. It also illustrates why burndown is useful for checking whether work is progressing toward the sprint goal. Because both sprints were simulated, the results should not be treated as a reliable real-world measure of long-term team velocity.

7. Conclusion

The Jira exercise converted the functional requirements of the Inter-City Freight Load Matching Marketplace into an organized Agile backlog with epics, prioritized user stories, and Fibonacci story points. Two sprints were planned and simulated, and the Burndown Chart was used to visualize remaining work. The exercise provided practical experience with backlog management, estimation, sprint execution, and progress tracking in Jira.
